


WATERMAIN SCHEDULE					
	Station	Description	Finished Grade	Top of Watermain	As Built Watermain
A	0+000.00	EXISTING TEE	105.45	103.05	
	0+014.50	EXISTING VB	105.61	103.21	
	0+015.48	45 BEND	105.63	103.23	
	0+028.20	SERVICE TEE	105.48	103.08	
	0+029.32	SERVICE TEE	105.47	103.07	
	0+030.64	SERVICE TEE	105.44	103.04	
	0+032.26	SERVICE TEE	105.42	103.02	
	0+046.05	SERVICE TEE	105.57	103.17	
	0+047.14	SERVICE TEE	105.57	103.17	
	0+048.42	SERVICE TEE	105.56	103.16	
B	0+050.06	SERVICE TEE	105.56	103.16	
	0+067.49	TEE	105.70	103.30	
	0+067.78	V BEND	105.71	103.31	
	0+068.28	V BEND *	105.73	103.79	
	0+070.88	V BEND *	105.81	103.79	
	0+071.38	V BEND	105.83	103.43	
	0+072.02	HYD TEE	105.86	103.46	
	0+082.25	SERVICE TEE	105.90	103.50	
	0+084.10	SERVICE TEE	105.88	103.48	
	0+086.07	SERVICE TEE	105.95	103.55	
C	0+100.90	TEE	105.97	103.57	
	0+103.63	SERVICE TEE	105.99	103.59	
D	0+104.10	CAP	106.05	103.65	
	0+000.00	TEE	105.70	103.30	
E	0+000.98	VB	105.69	103.29	
	0+001.23	11 BEND	105.69	103.29	
	0+001.40	V BEND	105.690	103.29	
	0+001.90	V BEND *	105.690	103.93	
	0+004.20	V BEND *	105.660	103.93	
	0+004.70	V BEND	105.660	103.26	
	0+057.80	SERVICE TEE	106.16	103.76	
	0+059.65	SERVICE TEE	106.17	103.77	
	0+075.60	SERVICE TEE	106.29	103.89	
	0+077.48	SERVICE TEE	106.31	103.91	
F	0+116.16	VB	107.45	105.05	
	0+121.89	TEE	107.43	105.03	
	0+000.00	TEE	105.97	103.57	
	0+001.28	V BEND	105.99	103.59	
	0+001.78	V BEND *	105.99	103.92	
	0+004.30	V BEND *	106.04	103.92	
	0+004.80	V BEND	106.05	103.65	
	0+012.15	11 BEND	106.28	103.88	
	0+019.04	SERVICE TEE	106.42	104.02	
	0+020.89	SERVICE TEE	106.42	104.02	
G	0+036.94	SERVICE TEE	106.31	103.91	
	0+038.74	SERVICE TEE	106.30	103.90	
	0+058.78	HYD TEE	106.47	104.07	
	0+061.54	SERVICE TEE	106.54	104.14	
	0+063.39	SERVICE TEE	106.59	104.19	
	0+079.40	SERVICE TEE	106.94	104.54	
	0+081.26	SERVICE TEE	106.94	104.54	
	0+088.35	SERVICE TEE	106.80	104.40	
	0+100.17	SERVICE TEE	106.79	104.39	
	0+116.14	SERVICE TEE	107.04	104.64	
H	0+117.98	SERVICE TEE	107.09	104.69	
	0+126.02	45 BEND	107.19	104.79	
	0+129.04	HYD TEE	107.20	104.80	
	0+131.68	45 BEND	107.19	104.79	
	0+137.70	SERVICE TEE	107.07	104.67	
	0+139.50	SERVICE TEE	107.06	104.66	
	0+155.48	SERVICE TEE	107.38	104.98	
	0+157.29	SERVICE TEE	107.40	105.00	
	0+162.50	TEE	107.43	105.03	
	0+175.58	SERVICE TEE	107.35	104.95	
I	0+177.38	SERVICE TEE	107.34	104.94	
	0+183.37	SERVICE TEE	107.50	105.10	
	0+185.17	SERVICE TEE	107.57	105.17	
	0+206.95	VB	107.81	105.21	
	0+212.76	V BEND	107.55	105.15	
	0+213.26	V BEND *	107.57	105.44	
	0+215.64	V BEND *	107.64	105.44	
	0+216.14	V BEND	107.64	105.24	
	0+218.95	TEE	107.56	105.16	
	0+218.95	TEE	107.56	105.16	

Pipe Interference Table			
Crossing No.	PIPE 1	PIPE 2	Clearance
1	WM Bottom 103.72	STM Top 103.22	0.50
2	WM Bottom 103.18	SAN Top 101.76	1.42
3	WM Bottom 103.47	STM Top 102.96	0.50
4	WM Bottom 103.58	SAN Top 101.94	1.64
5	WM Bottom 103.71	STM Top 103.21	0.50
6	WM Bottom 105.21	STM Top 104.72	0.50
7	WM Bottom 105.22	SAN Top 103.99	1.23
8	STM Bottom 102.79	SAN Top 101.68	1.11
9	STM Bottom 103.03	SAN Top 101.78	1.26
10	WM Bottom 103.03	SAN Top 101.67	1.39

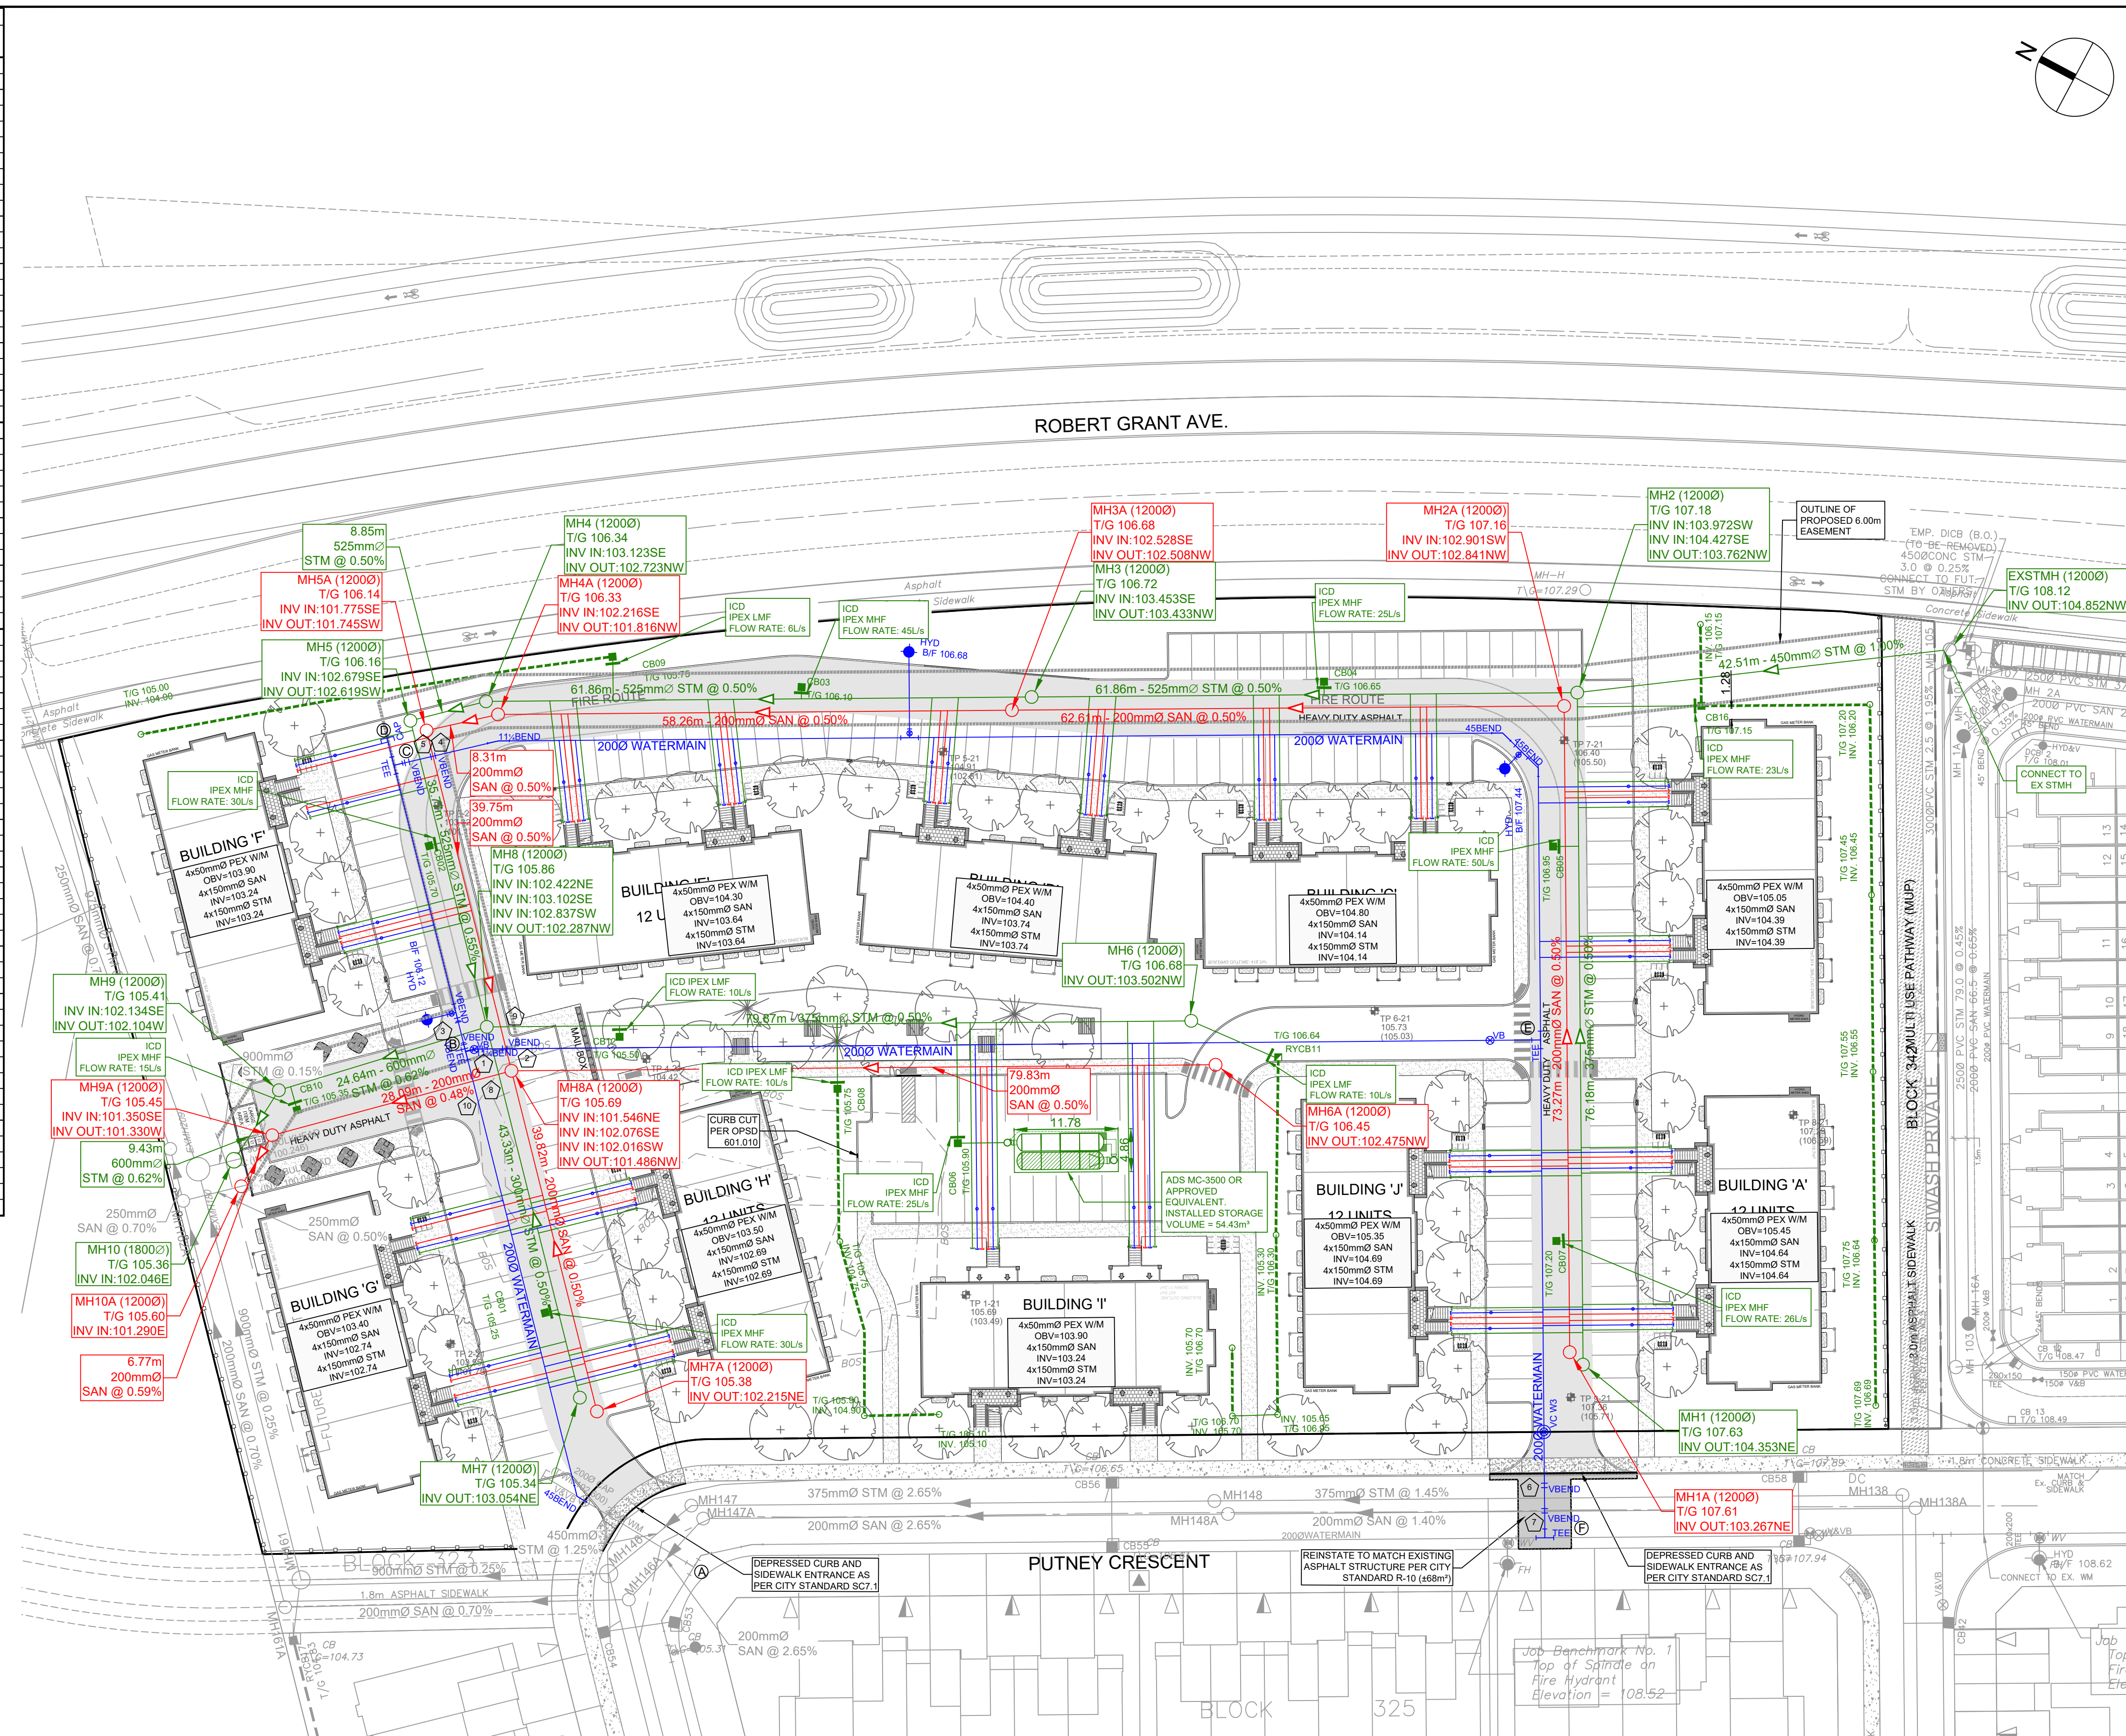

CLIENT

CLARIDGE HOMES

COPYRIGHT

This drawing has been prepared solely for the intended use, thus any reproduction or distribution for any purpose other than authorized by Arcadis is forbidden. Written dimensions shall have precedence over scaled dimensions. Contractors shall verify and be responsible for all dimensions and conditions on the job, and Arcadis shall be informed of any variations from the dimensions and conditions shown on the drawing. Shop drawings shall be submitted to Arcadis for general conformance before proceeding with fabrication.

Arcadis Professional Services (Canada) Inc.

Formerly BG Group Professional Services (Canada) Inc.

ISSUES

No.	DESCRIPTION	DATE
1	ISSUED TO CITY FOR REVIEW	2026.06.23
2	REVISED PER CITY COMMENTS	2026.09.23
3		
4		
5		

SEE 010 FOR NOTES, LEGEND, CB TABLE, STREET SECTIONS AND DETAILS

SITE BENCHMARK TO BE OBTAINED FROM LEGAL SURVEYOR ADV.

KEY PLAN

CONSULTANTS

SEAL

ARCADIS

333 Preston Street - Suite 500

Ottawa ON K1S 5N4 Canada

tel 613 225 1311

www.arcadis.com

PROJECT

CRT BLOCK 324

PROJECT NO:

30259740

DRAWN BY:

EH/MM

CHECKED BY:

RR

PROJECT MGR:

RM

APPROVED BY:

RM

SHEET TITLE

SERVICING PLAN

SHEET NUMBER

C-001

ISSUE

1
