
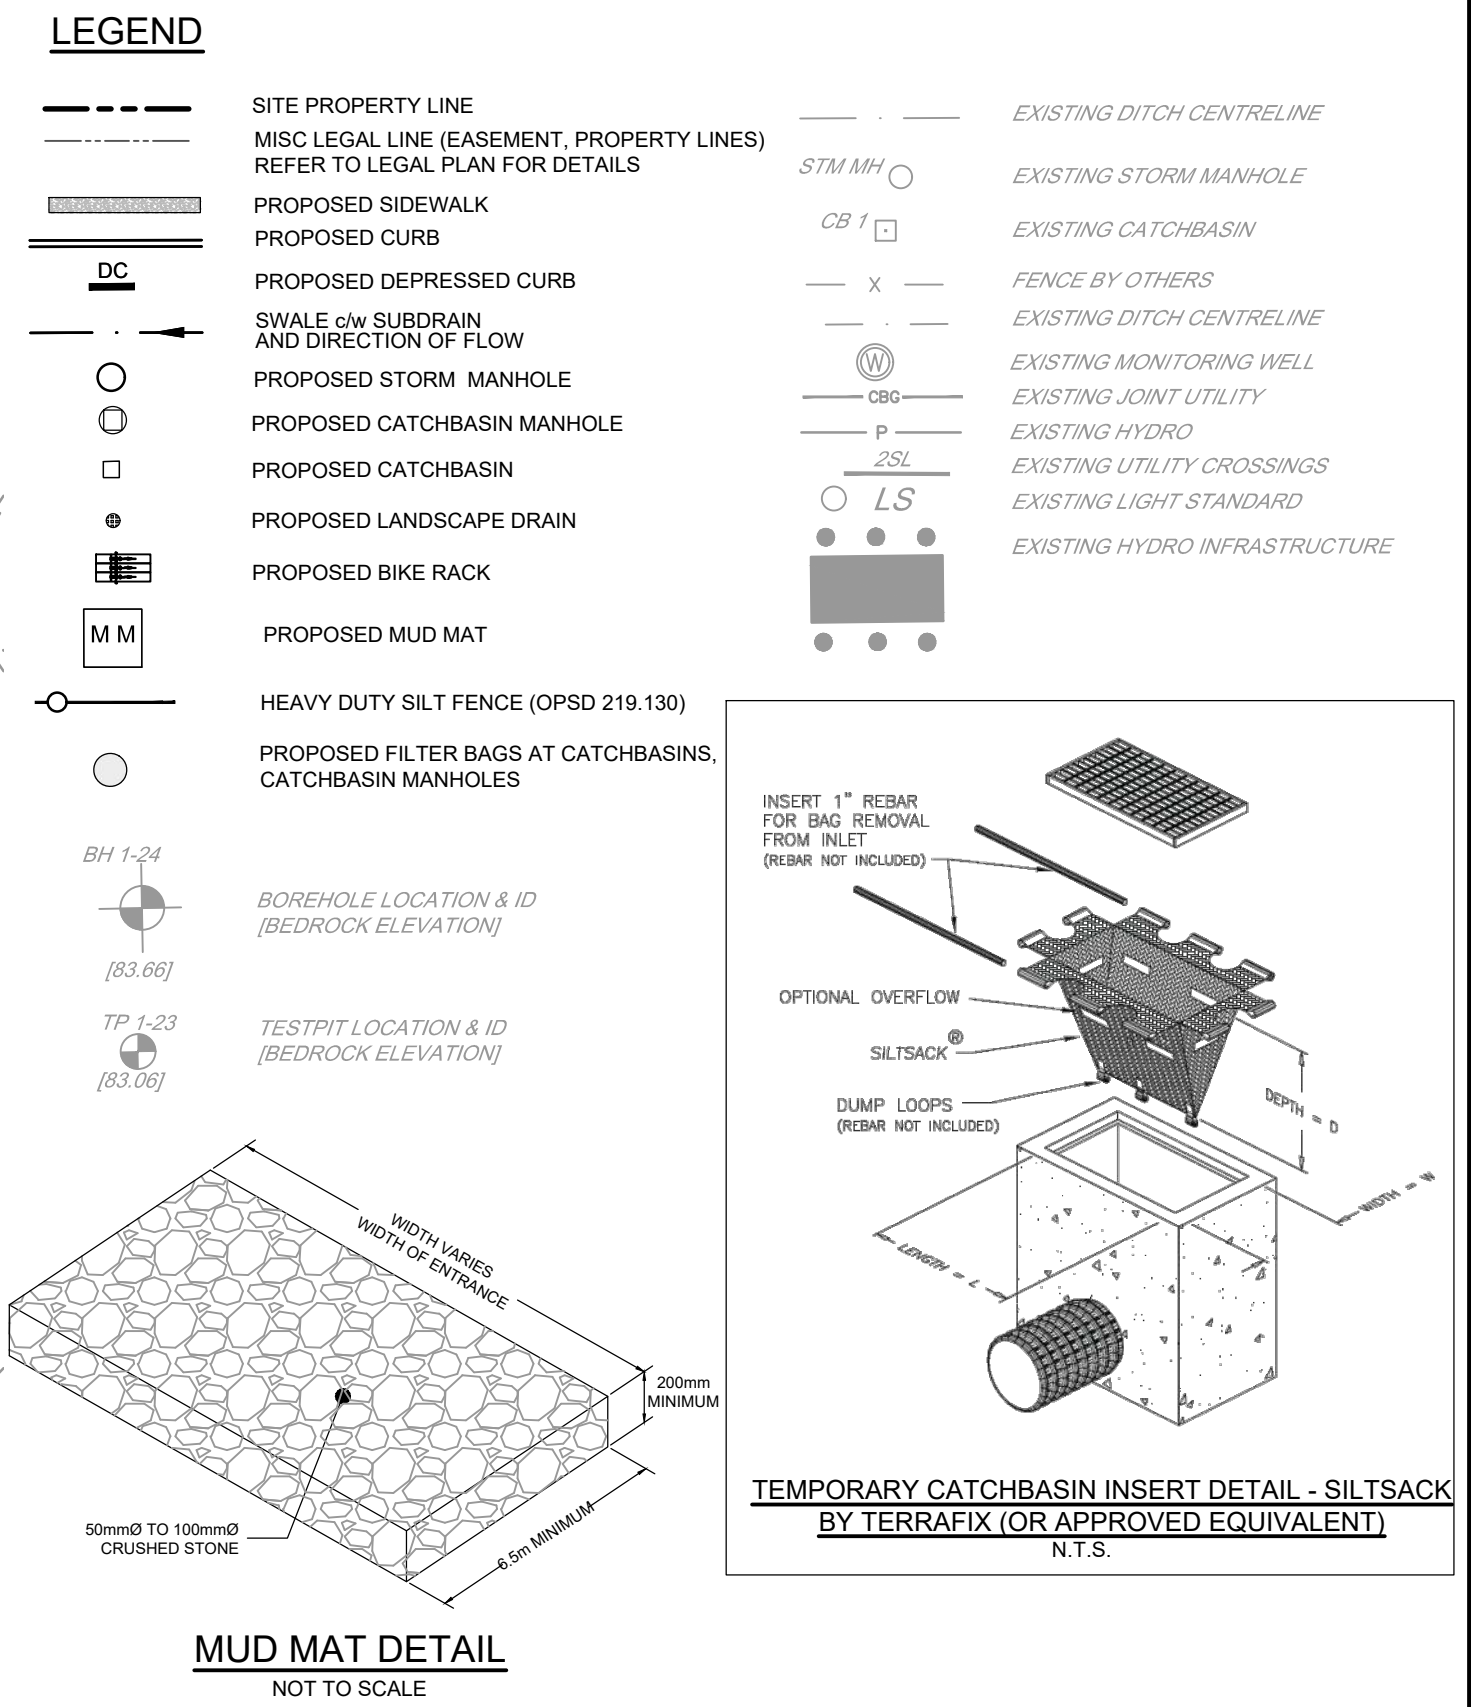
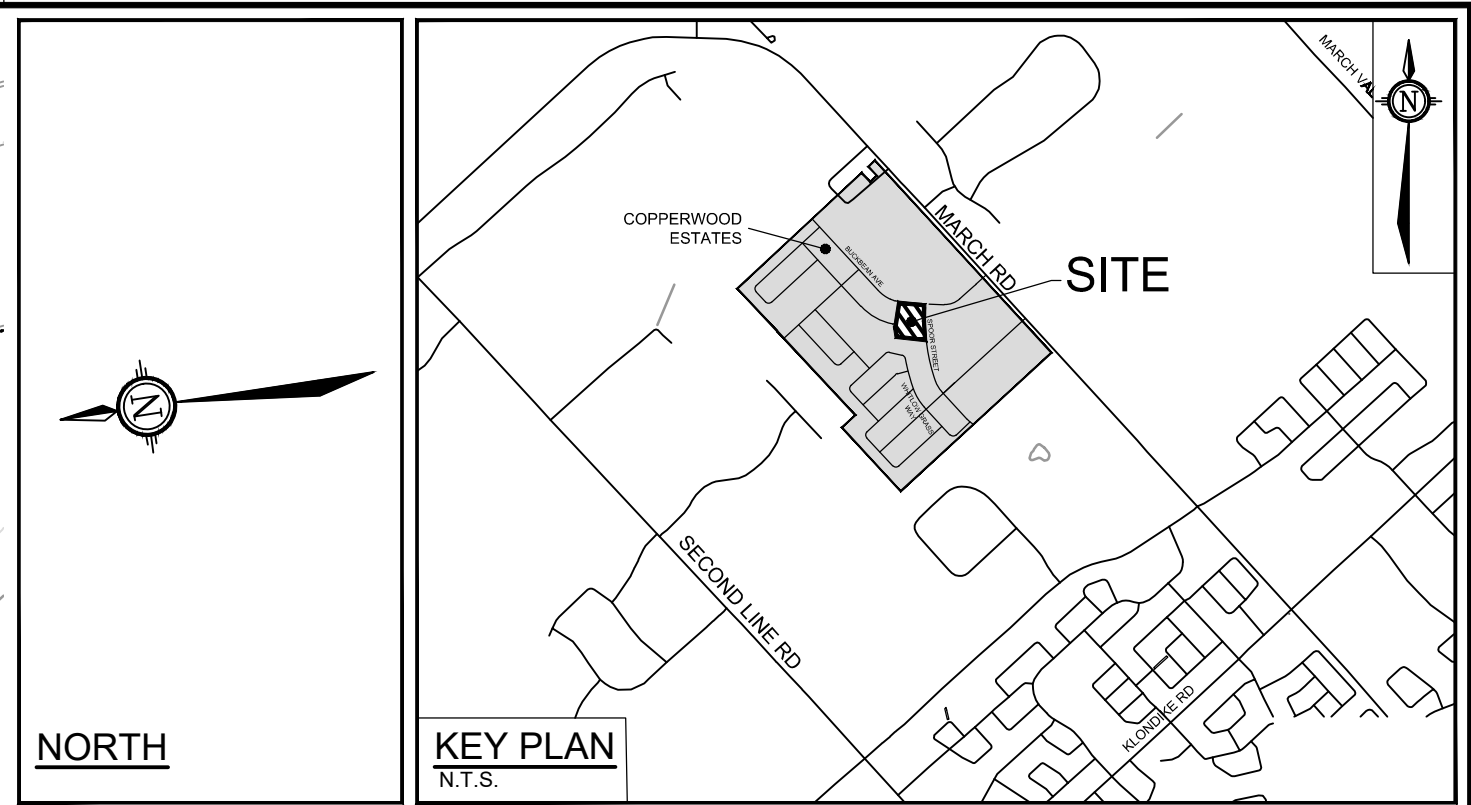


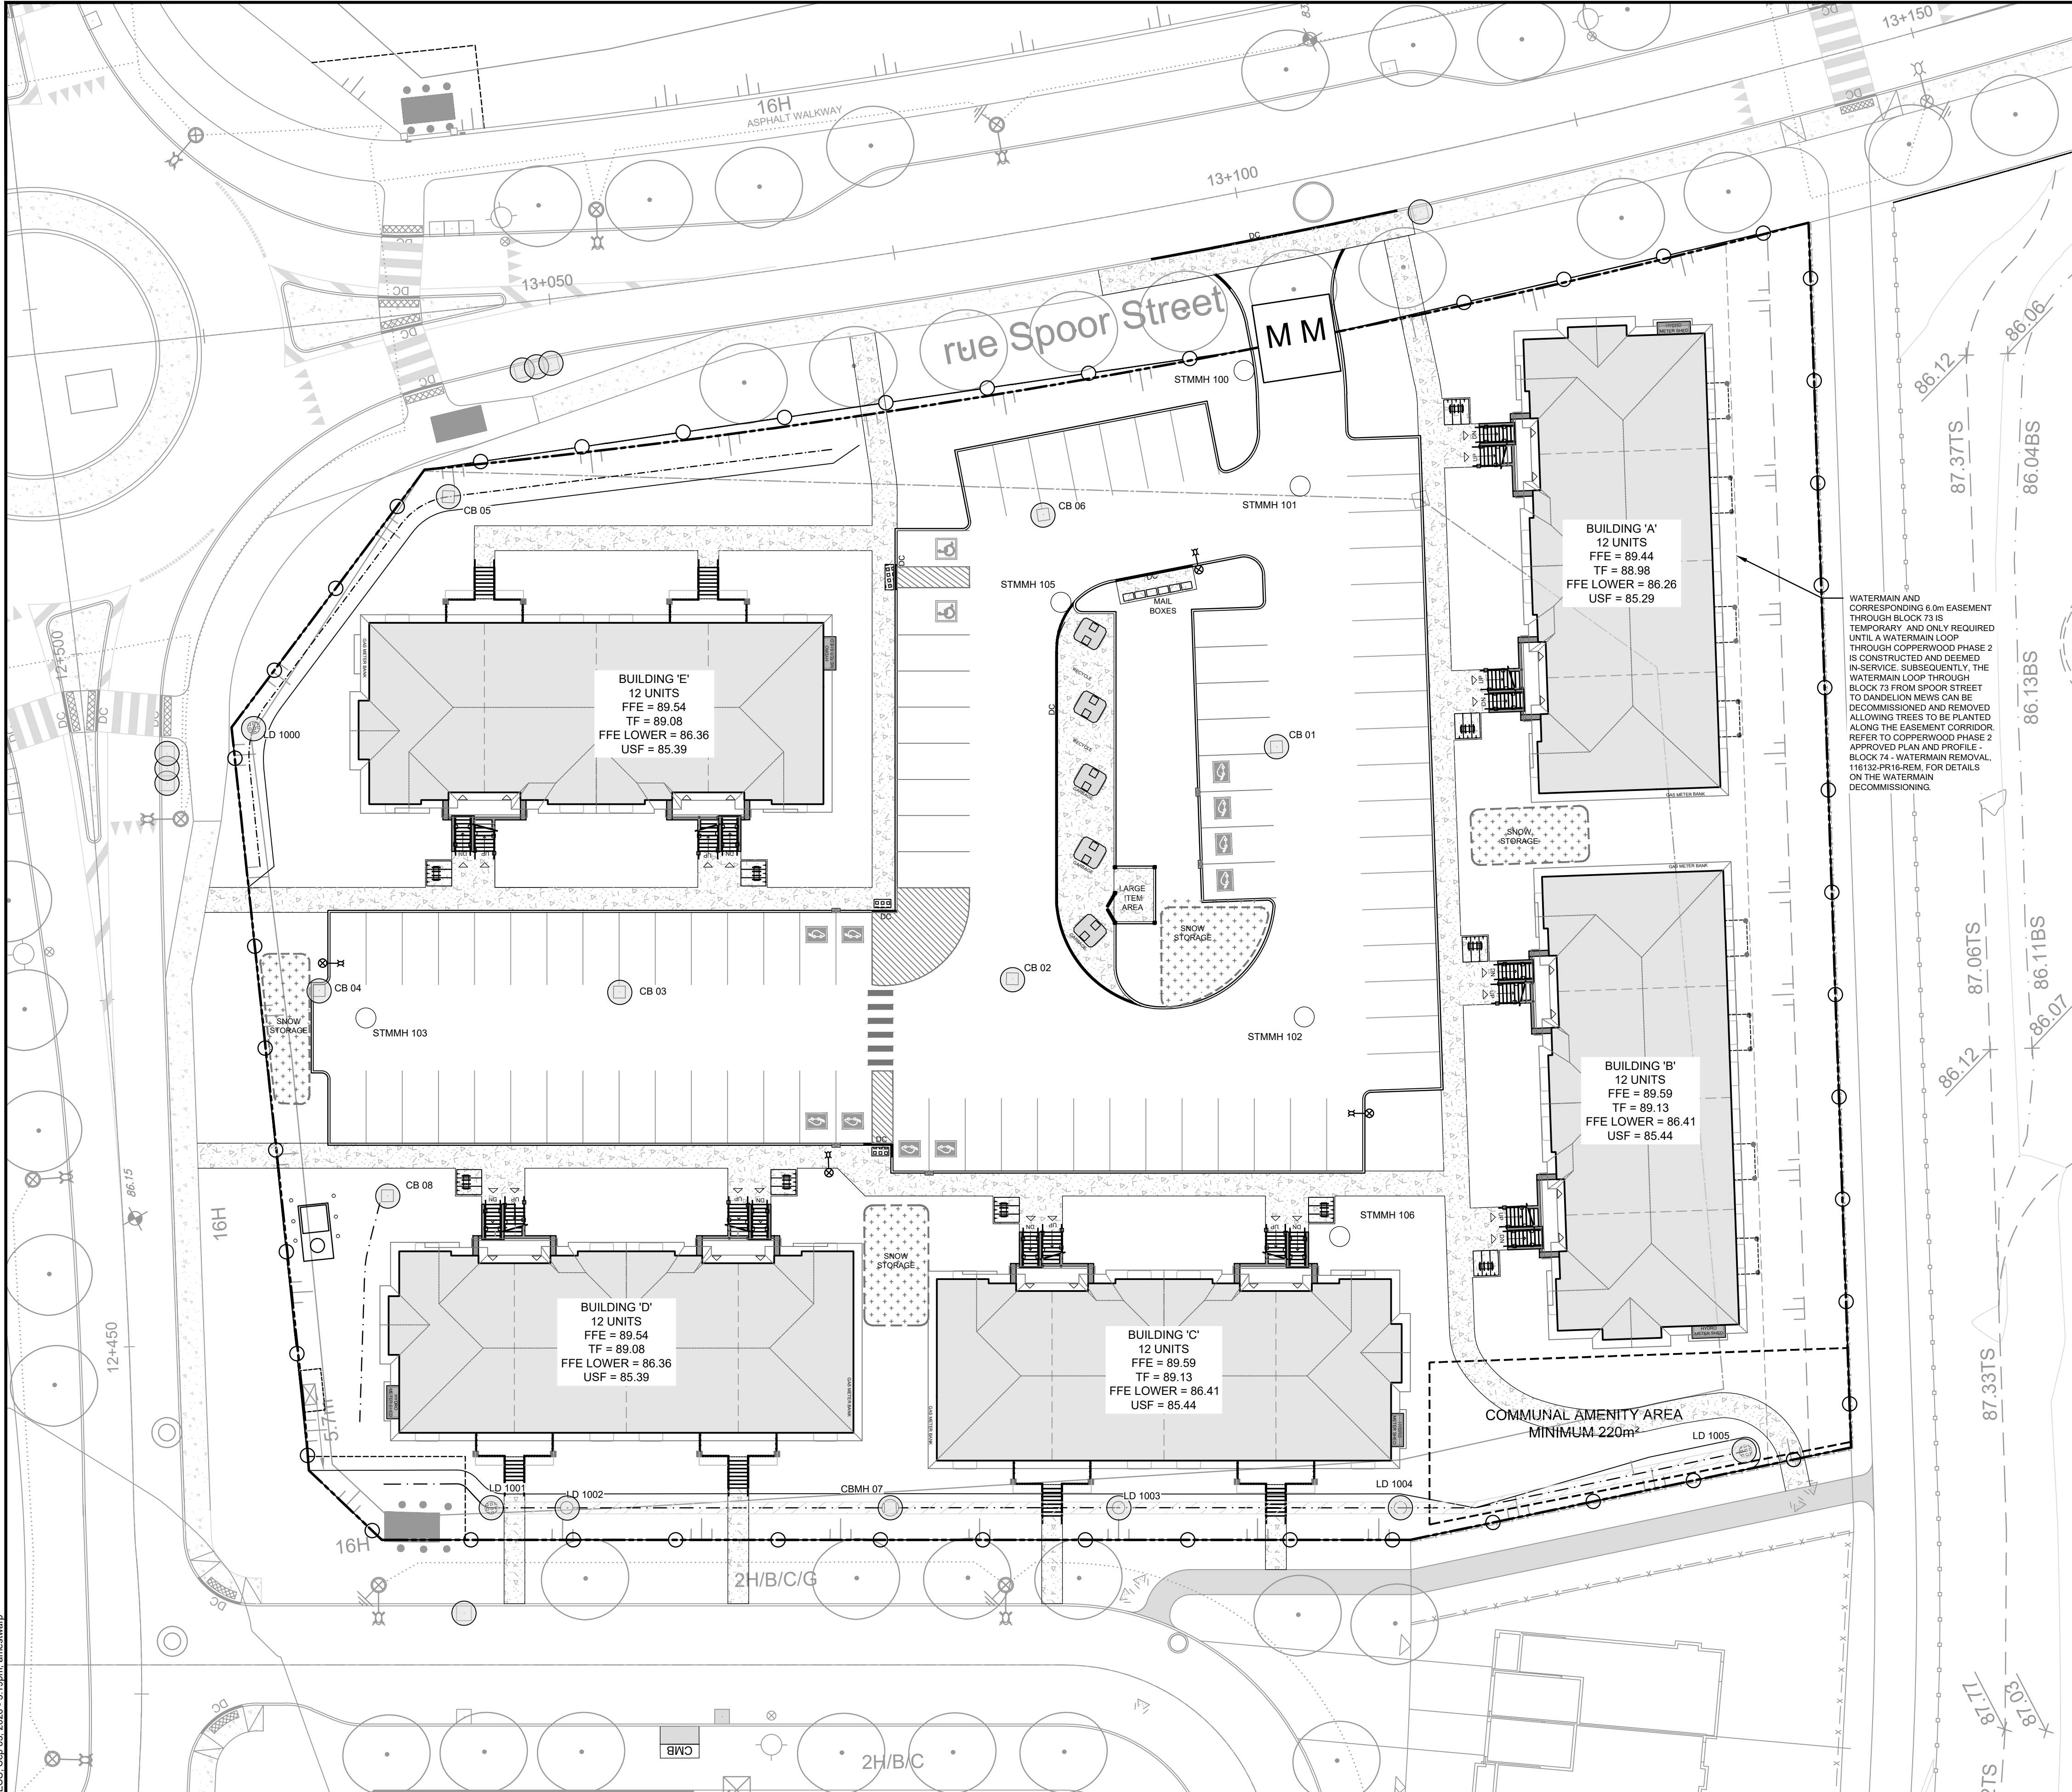


- EROSION AND SEDIMENT CONTROL NOTES:**
- THE CONTRACTOR SHALL IMPLEMENT BEST MANAGEMENT PRACTICES, TO PROVIDE FOR PROTECTION OF THE AREA DRAINAGE SYSTEM AND THE RECEIVING WATERCOURSE, DURING CONSTRUCTION ACTIVITIES. THE CONTRACTOR ACKNOWLEDGES THAT FAILURE TO IMPLEMENT APPROPRIATE EROSION AND SEDIMENT CONTROL MEASURES MAY BE SUBJECT TO PENALTIES IMPOSED BY ANY APPLICABLE REGULATORY AGENCY.
- THE OWNER AGREES TO PREPARE AND IMPLEMENT AN EROSION AND SEDIMENT CONTROL PLAN TO THE SATISFACTION OF THE CITY OF OTTAWA, APPROPRIATE TO THE SITE CONDITIONS, PRIOR TO UNDERTAKING ANY SITE ALTERATIONS (FILLING, GRADING, REMOVAL OF VEGETATION, ETC.) AND DURING ALL PHASES OF SITE PREPARATION AND CONSTRUCTION IN ACCORDANCE WITH THE CURRENT BEST MANAGEMENT PRACTICES FOR EROSION AND SEDIMENT CONTROL SUCH AS BUT NOT LIMITED TO INSTALLING FILTER CLOTHS ACROSS MANHOLE/CATCHBASIN LIDS TO PREVENT SEDIMENTS FROM ENTERING STRUCTURES AND INSTALL AND MAINTAIN A HEAVY DUTY SILT FENCE BARRIER AS REQUIRED.
 - IT WILL BE THE RESPONSIBILITY OF THE CONTRACTOR TO SUBMIT A DETAILED CONSTRUCTION SCHEDULE AND APPROPRIATE STAGING, DEWATERING AND EROSION AND SEDIMENT CONTROL PLANS TO THE CONTRACT ADMINISTRATOR FOR REVIEW AND APPROVAL PRIOR TO THE COMMENCEMENT OF WORK. A COPY OF THE CITY OF OTTAWA SPECIAL PROVISION F-1004 WILL BECOME PART OF ANY CONTRACT AND WHICH OUTLINES THE CONTRACTUAL REQUIREMENTS WHICH INCLUDES PREPARATION OF A DETAILED EROSION AND SEDIMENT CONTROL PLAN.
 - THE CONTRACTOR SHALL PLACE FILTER BAGS UNDER THE CATCHBASIN AND MANHOLE GRATES FOR THE DURATION OF CONSTRUCTION AND WILL REMAIN IN PLACE DURING ALL PHASES OF CONSTRUCTION, SITE DEMOBILIZATION AND REMAIN IN PLACE UNTIL SITE STABILIZATION IS ACHIEVED.
 - SILT FENCING FOR ENTIRE PERIMETER OF SITE, SHALL BE UTILIZED TO CONTROL EROSION FROM THE SITE DURING CONSTRUCTION, SITE DEMOBILIZATION AND REMAIN IN PLACE UNTIL SITE STABILIZATION IS ACHIEVED.
 - THE CONTRACTOR ACKNOWLEDGES THAT FAILURE TO IMPLEMENT EROSION AND SEDIMENT CONTROL MEASURES MAY BE SUBJECT TO PENALTIES IMPOSED BY ANY APPLICABLE REGULATORY AGENCY.
 - PROVIDE MUD MATS AT ALL CONSTRUCTION ACCESS POINTS TO MINIMIZE SEDIMENT TRANSPORT OFFSITE.
 - EROSION AND SEDIMENT CONTROL MEASURES MAY BE MODIFIED IN THE FIELD AT THE DISCRETION OF THE CITY OF OTTAWA SITE INSPECTOR OR CONSERVATION AUTHORITY.


REFER TO 125113-ND1 FOR ADDITIONAL NOTES & DETAILS

NOTE:
THE POSITION OF ALL POLE LINES, CONDUITS, WATERMANS, SEWERS AND OTHER UNDERGROUND AND OVERGROUND UTILITIES AND STRUCTURES IS NOT NECESSARILY SHOWN ON THE CONTRACT DRAWINGS, AND WHERE SHOWN, THE ACCURACY OF THE POSITION OF SUCH UTILITIES AND STRUCTURES IS NOT GUARANTEED. BEFORE STARTING WORK, DETERMINE THE EXACT LOCATION OF ALL SUCH UTILITIES AND STRUCTURES AND ASSUME ALL LIABILITY FOR DAMAGE TO THEM.

No.	REVISION	DATE	BY
3.	REVISED PER CITY COMMENTS	SEPT 04/2026	ARM
2.	REVISED PER CITY COMMENTS	JULY 23/2026	ARM
1.	ISSUED FOR SPA	APRIL 08/2026	ARM

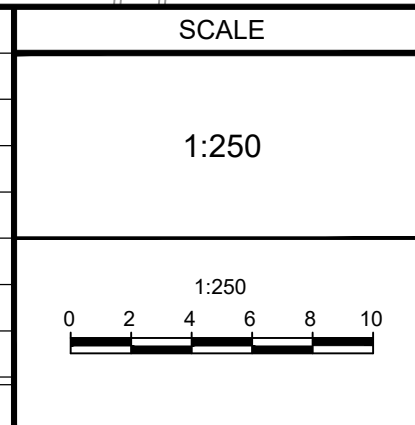

DESIGN	AM
CHECKED	ARM
DRAWN	AM
CHECKED	ARM
APPROVED	GJM



NOVATECH
Engineers, Planners & Landscape Architects
Suite 200, 240 Michael Cowpland Drive
Ottawa, Ontario, Canada K2M 1P6
Telephone (613) 254-9643
Facsimile (613) 254-5867
Website www.novatech-eng.com

LOCATION 1100 SPOOR STREET, CITY OF OTTAWA COPPERWOOD ESTATES (BLOCK 73)	
DRAWING NAME EROSION AND SEDIMENT CONTROL PLAN	
PROJECT No. 125113	REV #3
DRAWING No. 125113-ESC	

M:\2025\125113\CADD\DWG\125113-ESC.dwg, ESC, Sep 03, 2026 - 5:19pm, ameswarp

CITY FILE No.D07-12-26-0035
